Ð

## **Arterial BRT Update**








Katie Roth, Project Manager 612-349-7772 katie.roth@metrotransit.org Transportation Committee April 11, 2016




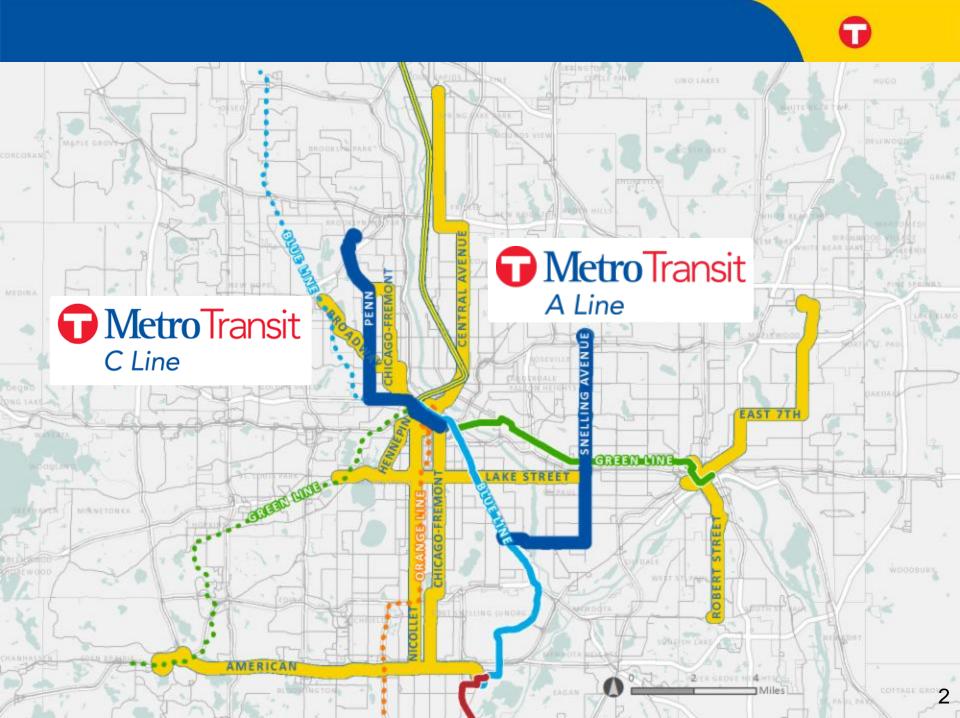

## THE A LINE OPENS JUNE 11

61	
DAYS	

- A Line service begins every 10 minutes
- Route 84 reduced to 30-minute service
- No other related service changes
- Launch & community celebrations

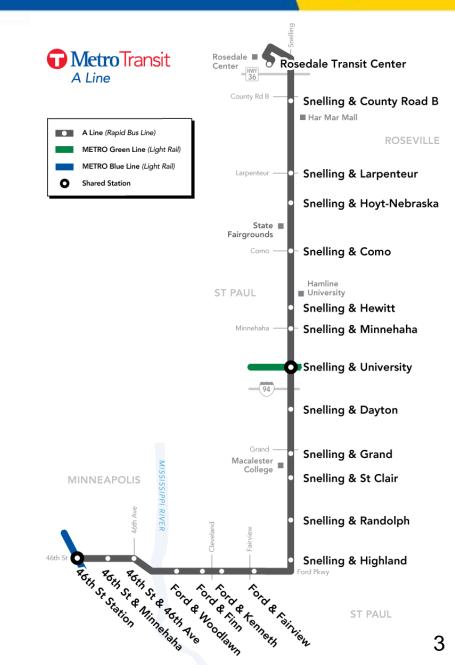

## **Getting ready for June 11: Building the line**





Ongoing construction and testing



Operations and training procedures development



Fare collection equipment installation



4

## **Getting ready for June 11: Building excitement**



#### Community tour – March 9

Marketing plans underway

Metro Transit unveils Bus Rapid Transit



#### Growing news coverage



#### Macalester College – March 29



# G


## **C** Line Activities



- Final station plan approval
- Environmental review
- Design & engineering initiation
- Study of potential long-term (Phase II) Glenwood Avenue realignment
- Full funding pursuit



# **C** Line Station Plan

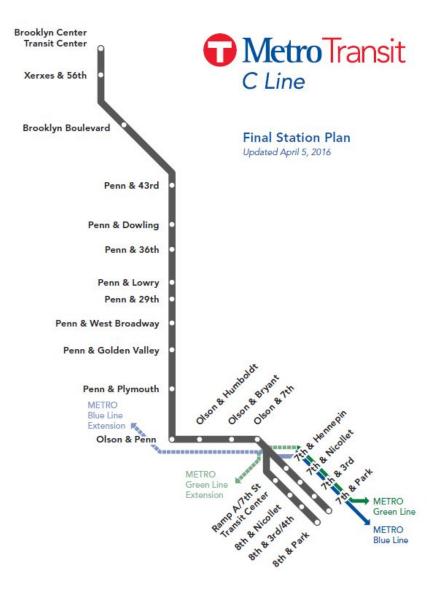

#### • Nov. 2015: Draft

- Published November 6, 2015
  Comments accepted through
  December 20
- Over 150 comments received

## • Feb. 2016: Recommended


Released for Public Comment
 February 10
 Comments accepted through
 March 11

## • April 2016: Final

 Presented for approval in Business Item 2016-70



## **C Line / Penn Avenue Design Coordination**

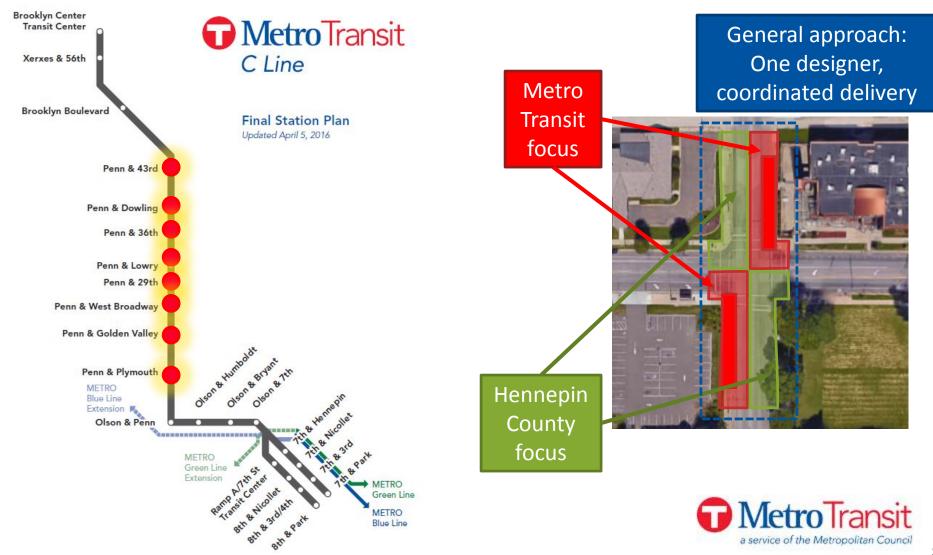

# Ð

## **Revised C Line Project Timeline**

	2015	2016	2017	2018	2019	
Planning	Metropolitan Council Station Plan Approval					
Design / Engineering						
Construction Pending Full Project Funding						
Open C Line		Opening date	 to be determined 	in construction pl	nase	


- Shift construction from 2017 to 2018
  - Full funding not identified for 2017
  - Initiate design mid-2016; 12-18 months of plan preparation
  - Potential for better coordination with other corridor construction projects






Ð

## **Glenwood Avenue**

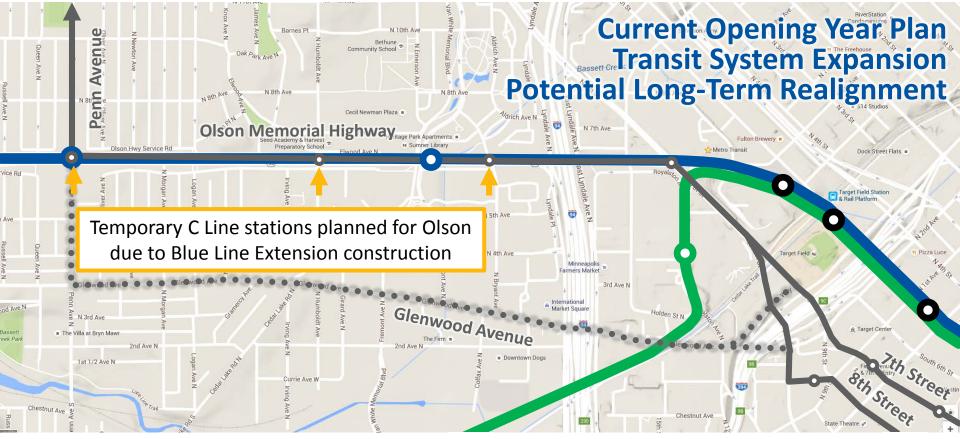

Not shown: Potential bus network modifications related to Green Line Extension & Blue Line Extension. Plans TBD as implementation nears.



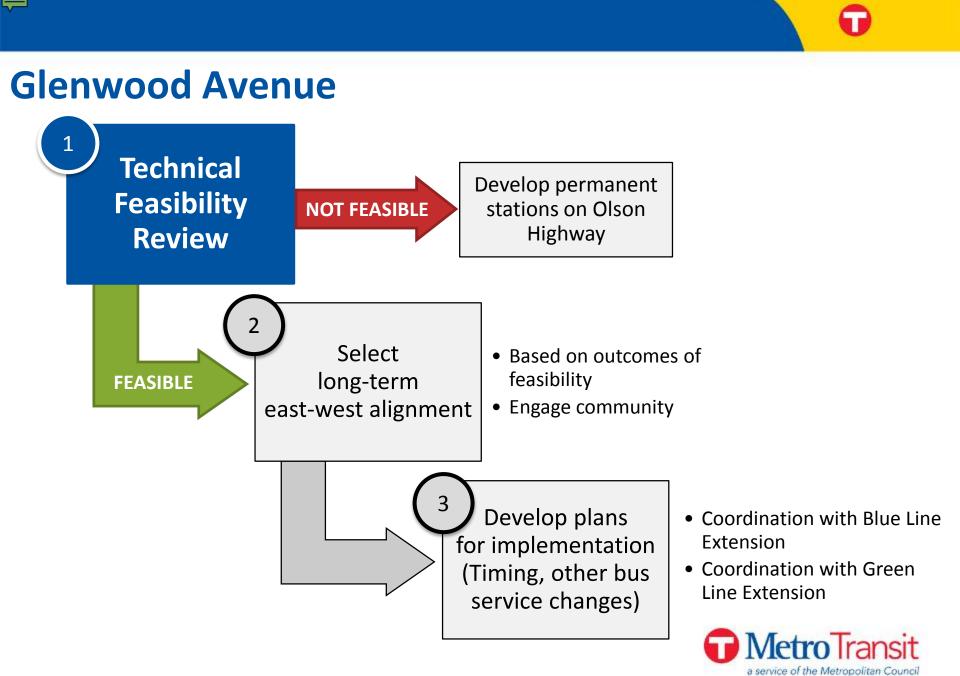


## metrotransit.org/a-line metrotransit.org/c-line-project



Katie Roth, Project Manager 612-349-7772 katie.roth@metrotransit.org Transportation Committee April 11, 2016



## 2016-70: Final C Line Station Plan

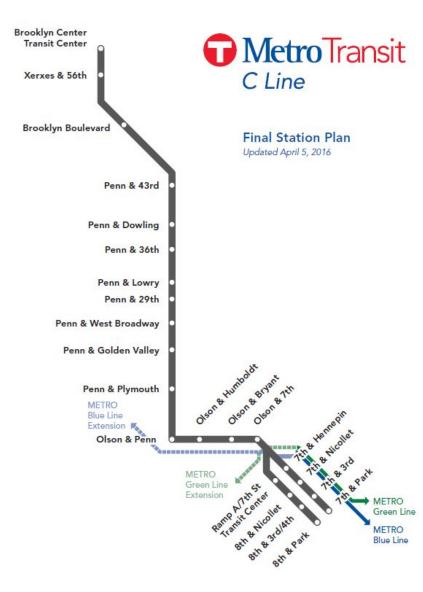

#### • Nov. 2015: Draft

- Published November 6, 2015
  Comments accepted through
  December 20
- Over 150 comments received

#### • Feb. 2016: Recommended

Released for Public Comment
 February 10
 Comments accepted through
 March 11

### • April 2016: Final

 Presented for approval in Business Item 2016-70



## 2016-71: C Line Hennepin County Agreement

